



# RAJASTHAN PROGRESS REPORT

May 2020



## SEWA INTERNATIONAL TOILET AND HYGIENE PROJECT FOR A GIRL CHILD

**SUPPORTED BY:**  
**SODHANI FOUNDATION**  
(Smt. Mona Khaitan and Shri Vishwanath Khaitan)  
Shri Arvind Sodhani

# Initial Need Analysis

**Table 1: List of schools in Sikar district with the number of beneficiaries and the number of toilets with the project status (24 toilets are in progress)**

S.No.	Name of the school	Region	Total	No of toilets required	Project details	Project Status
1	Uchha Madhyamik Vidya Mandir	Sawbly Marg, Sankul, Sikar	220	4	Phase 1	In progress
2	Upper Primary Adarsh Vidya Mandir	Mathura Basti, Sankul, Sikar	80	4	Phase 1	In progress
3	Shri Madanlal Biyani Ucha Madhyamik Balika Adarsh Vidya Mandir	Rishikul Marg, Sankul, Sikar	64	8	Phase 1	In progress
4	Shri. Bala Vais Viyani Prathamik Adarsh Vidya Mandir	Rishikul Marg, Sankul, Sikar	83		Phase 1	In progress
5	Rajkia Ucha Madhamik Vidyalay	Laxmangarh, Sikar	80	4	Phase 2	Yet to Start
6	Raghukul High Sec. School	Laxmangarh, Sikar	850	8	Phase 1	In progress
7	Shri Saraswati Sec. School	Laxmangarh, Sikar	1025	8	Phase 2	Yet to Start
8	Gov. Sr Sec School	Laxmangarh, Sikar	250	8	Phase 2	Yet to Start
9	Gov Bhadech Sec School	Laxmangarh, Sikar	300	6	Phase 2	Yet to Start
		<b>Total</b>	<b>2952</b>	<b>50</b>		


Note: We have made a few changes to the list. In the last report, we had mentioned about building 8 toilets each in school 3 and 4. (Co-ordinator mentioned School 3 and 4 share the compound, they have built 8 unit toilet block which will be used by both the schools. ) **Schools that are under construction, 80% of the work is finished. The pending work is Painting, doors, roof, and donor name installation.**

# Project Location

\*The aerial distance from New Delhi to Jaipur is 241 km while the road distance between New Delhi to Jaipur is 268 km.



The road distance between Jaipur to Sikar District is 114 km.

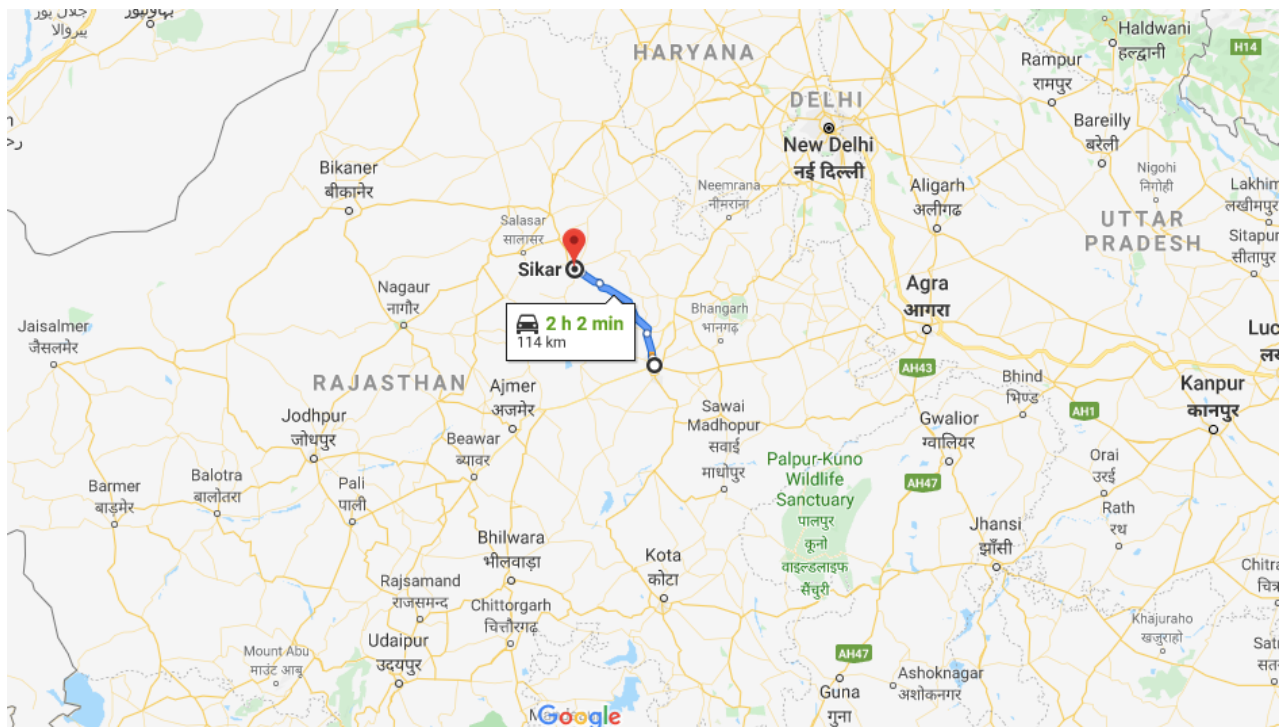

# Under Construction

---



# Covid 19 Lockdown - Brief Info

---

On 24 March 2020, the Government of India ordered a nationwide lockdown for 21 days. On 14 April, the nationwide lockdown extended until 3 May, with a conditional relaxations after 20 April for the regions where the spread had been contained or was minimal.

On 1 May, the Government of India extended the nationwide lockdown further by two weeks until 17 May. The Government divided all the districts into three zones based on the spread of the virus—green, red and orange—with relaxations applied accordingly. On 17 May, the lockdown was further extended till 31 May by the National Disaster Management Authority.

**On May 30th, it was announced that the ongoing lockdown would be further extended till 30th June in containment zones, with services resuming in a phased manner starting from 8th June.**

**Red Zones:** There is a restriction on all activities in these areas.

**Orange Zones:** Limited transport and restricted services and activities.

**Green Zones:** All activities except those prohibited nationwide will be allowed.

**Within Red Zones and Orange Zones, district authorities will identify clusters (colonies/wards/towns in urban centres and villages/panchayats/blocks in rural areas) as containment zones where life will be severely restricted..**

**Note: Sikar District of Rajasthan is placed under Orange zone with few of our schools selected for construction have been declared as containment zone. Work can be resumed by Mid June, according to the district authorities.**

# Project completion schedule

---

## **Challenges post Lockdown:**

1. Shortage of Workers (Migrant workers have moved back to their natives across India)
2. Situations can change anytime due to covid 19 and permission to resume work can be withdrawn.

## **Planned activities:**

1. Our Local co-ordinators are well connected with District authorities and will be working towards the completion of the project with all the resources available to them in the current situation.
  2. The current Vendor will finish the remaining work of Phase1 as soon as the restrictions are lifted.
  3. In Parallel, another vendor will be hired to initiate phase 2 so, we can finish the project as scheduled.
- 
