

# RAJASTHAN PROGRESS REPORT



August 2020



**SEWA INTERNATIONAL  
TOILET AND HYGIENE PROJECT FOR A GIRL  
CHILD**

**SUPPORTED BY:  
SODHANI FOUNDATION**  
(Smt. Mona Khaitan and Shri Vishwanath Khaitan)  
Shri Arvind Sodhani

# Initial Need Analysis

**Table 1: List of schools in Sikar district with the number of beneficiaries and the number of toilets with the project status**

S.No.	Name of the school	Region	Total	No of toilets/Urinal	Project details	Project Status
1	Uchha Madhyamik Vidya Mandir	Sawbly Marg, Sankul, Sikar	220	2 Toilets 2 Urinals	Phase 1	In Progress - doors, painting, taps
2	Upper Primary Adarsh Vidya Mandir	Mathura Basti, Sankul, Sikar	80	2 Toilets 2 Urinals	Phase 1	In Progress - doors, painting, taps
3	Shri Madanlal Biyani Ucha Madhyamik Balika Adarsh Vidya Mandir	Rishikul Marg, Sankul, Sikar	64	8 Toilets 8 Urinals	Phase 1	In Progress - doors, painting, taps, sanitary fittings in toilets at ground floor
4	Shri. Bala Vais Viyani Prathamik Adarsh Vidya Mandir	Rishikul Marg, Sankul, Sikar	83		Phase 1	
5	Rajkia Ucha Madhamik Vidyalay	Laxmangarh, Sikar	80	2 Toilets 2 Urinals	Phase 2	In progress
6	Raghukul High Sec. School	Laxmangarh, Sikar	850	6 Toilets	Phase 1	Structure is completed. In progress - Sanitary work, door, roof and painting
7	Shri Saraswati Sec. School	Laxmangarh, Sikar	1025	4 Toilets	Phase 2	In Progress - doors, painting, taps
8	Gov. Sr Sec School	Laxmangarh, Sikar	250	4 Toilets 4 Urinals	Phase 2	Start Date: Aug last week
9	Rajkeey uchch primary sanskrit school	Laxmangarh, Sikar		3 Toilets 3 Urinals	Phase 2	Start Date: Aug last week
		<b>Total</b>	<b>2652</b>	<b>52</b>		

Note: We have made a few changes to the list. We have replaced Govt Bhadech sec school with Rajkeey uchch primary Sanskrit school. The current team of 6 workers who were working on Phase 1 of the project have resumed work. We assembled an additional team to work in Phase 2 schools. Both the teams, are working in parallel. We are aiming to finish Phase 1 by August last week and Phase 2 by September..




# Project Location

\*The aerial distance from New Delhi to Jaipur is 241 km while the road distance between New Delhi to Jaipur is 268 km.



The road distance between Jaipur to Sikar District is 114 km.

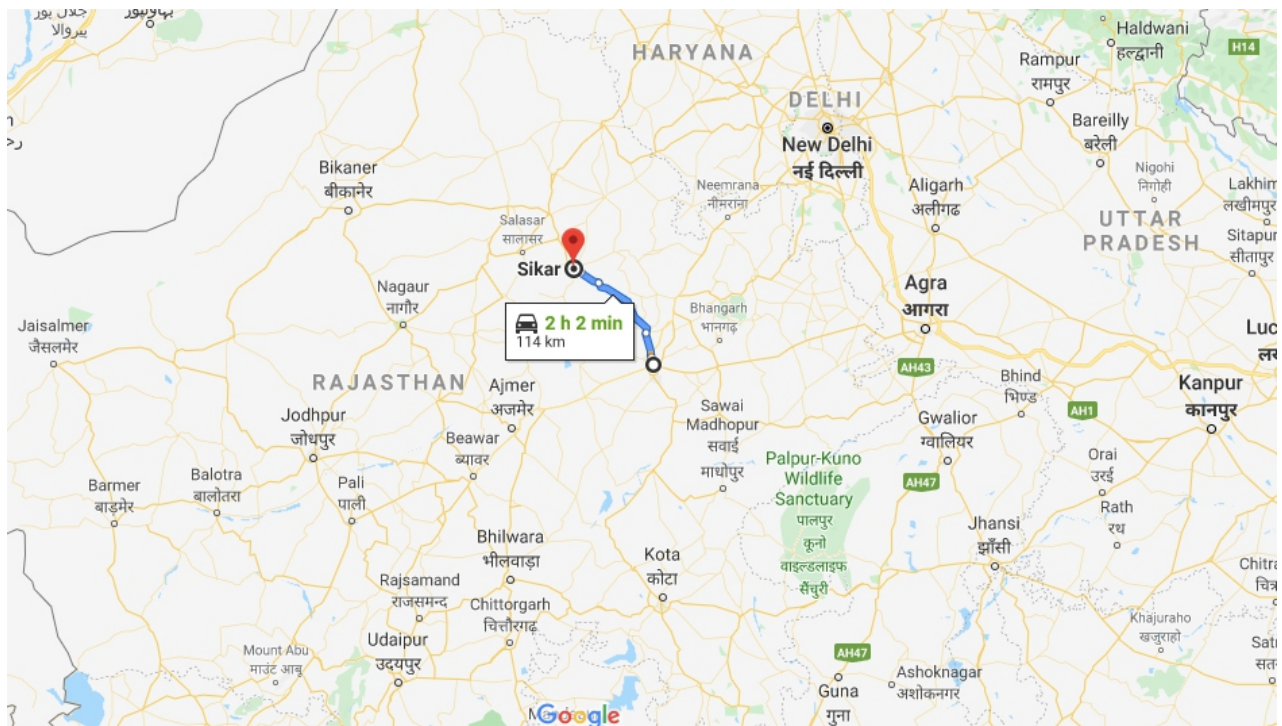




# Shri Sarswati Sec. School - Phase 2





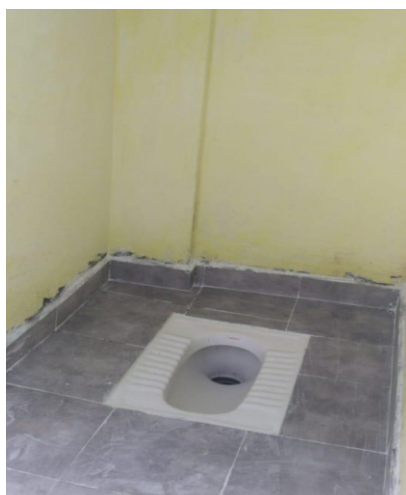



# Upper Primary Adarsh Vidya Mandir - Phase 1





# Uchha Madhyamik Vidya Mandir - Phase 1

---





# Rajkia Ucha Madhamik Vidyalay - Phase 2





# Raghukul High Sec. School - Phase 1





# BACK TO SCHOOL

---

**As schools are scheduled to re-open amidst increasing cases of Covid-19, the Sewa team is ensuring we reach out to school authorities to extend our services to keep our children safe. Sewa is ensuring the following safety measures :**

1. Masks for all students
2. Hand wash area
3. Equipped medical assistance
4. Health & Hygiene awareness
5. Sanitising the classrooms
6. Installing sanitizer units

Thank You for supporting us,  
Sewa T&H Team  
[www.toilets-sewauasa.org](http://www.toilets-sewauasa.org)
