



**PROJECT COMPLETION REPORT
(LUCKNOW & GORAKHPUR: UTTAR PRADESH)**

**Sewa International
Toilet and Hygiene Project for a girl child**

Supported by: Riya Dadheech

Initial Need Analysis Data - Uttar Pradesh

Table 1: List of schools in Lucknow and Gorakhpur districts with the number of beneficiaries and the number of non-functional toilets

S.No.	Region	Name of the school	No of boys	No of girls	Total	No of toilets Under repair work
1	Lucknow	Primary School Baldi kheda Zone1	72	43	115	2
2	Lucknow	Primary School Mukarim nagar	55	59	114	2
3	Lucknow	Junior Bauauli Khalilabad	62	59	121	2
4	Lucknow	Primary School Faizullah Ganj	103	99	202	2
5	Lucknow	Primary School Amrayigaun	42	47	89	2
6	Lucknow	Primary School Bauauli Khalilabad	60	75	135	2
7	Gorakhpur	Seehapaar High School	21	18	39	1
8	Gorakhpur	Rajkeey abhinav vidhyalaya	190	160	350	2
9	Gorakhpur	Rajkeey high school, varansi bypass	40	54	94	1
10	Gorakhpur	Government girls inter collage	0	950	950	3
11	Gorakhpur	Rajkeey inter collage pipriganj	0	864	864	8
		Total	645	2428	3073	27

Note: We have made a few changes in the list of schools selected for the sewa toilet project in Lucknow and Gorakhpur. We have replaced few schools from the allotted list as the school administration received funds from the other sources. (Refer table 2 for more details)

Completed Project List - Uttar Pradesh


Table 2: List of schools in Lucknow and Gorakhpur districts with the number of beneficiaries and the number of toilets/urinals/washbasins

S.No.	Region	Name of the school	Total	No. of toilets/urinals	Project Details	Status of work
1	Lucknow	Primary School Baldi kheda Zone1	117	2	Toilet and Wash Basins repair and renovation	Completed
2	Lucknow	*Primary School Pancham kheda 2, Zone-1	155	4	Toilet repair and renovation	Completed
3	Lucknow	Junior Bauauli Khalilabad	121	2	Toilet repair and renovation	Completed
4	Lucknow	*Primary School Bauauli Khalilabad	135	2	Toilet repair and renovation	Completed
5	Lucknow	Primary School Amrayigaun	89	3	Toilet and Bathroom repair and renovation	Completed
6	Gorakhpur	*Rajkey High School Gahira	126	11	Toilet and 3 new Wash Basins repair and renovation	Completed
7	Gorakhpur	*Primary school Jattepur Uttari	136	2	Toilet repair and renovation	Completed
8	Gorakhpur	*Primary school Hazaripur Naveen	100	2	Toilet repair and renovation	Completed
9	Gorakhpur	*Champa Devi Govt. Girls Inter College, Harnahi	846	11	Toilet and 7 new Wash Basins repair and renovation	Completed
		Total	1825	39		


Note: * represents new schools

Project Location

*The aerial distance from New Delhi to Lucknow is 420 km while the road distance between New Delhi to Lucknow is 554 km.



*The aerial distance from New Delhi to Gorakhpur is 644 km while the road distance between New Delhi to Gorakhpur is 822 km.

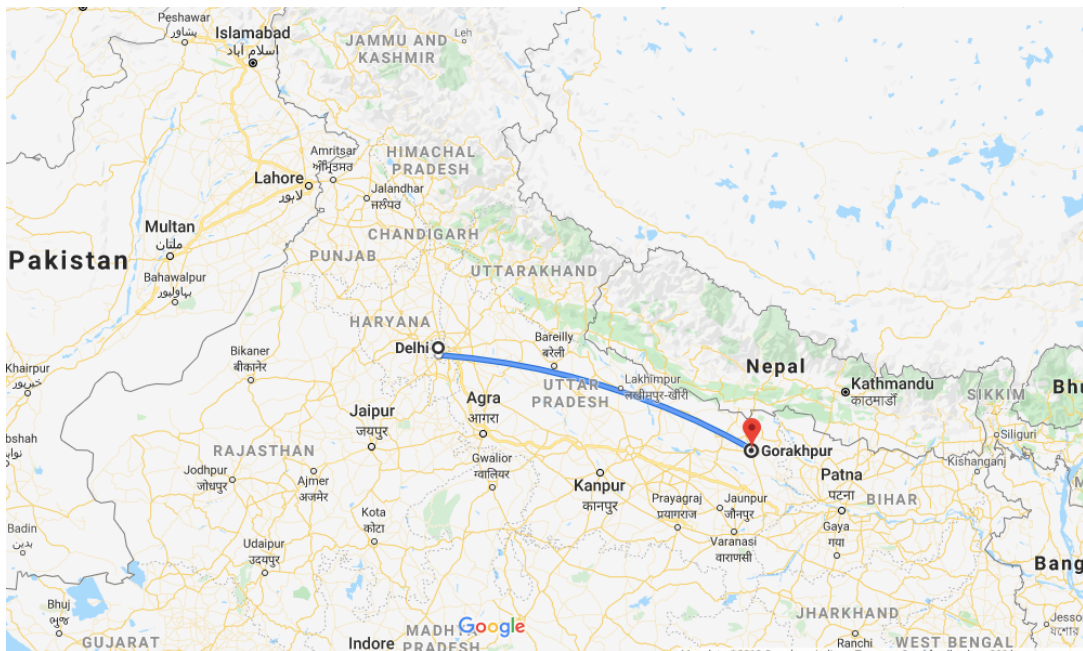

Under Construction Pictures




Project Completion Pictures



Our Success Story

www.toilets-sewausea.org/videos

Click on the below image

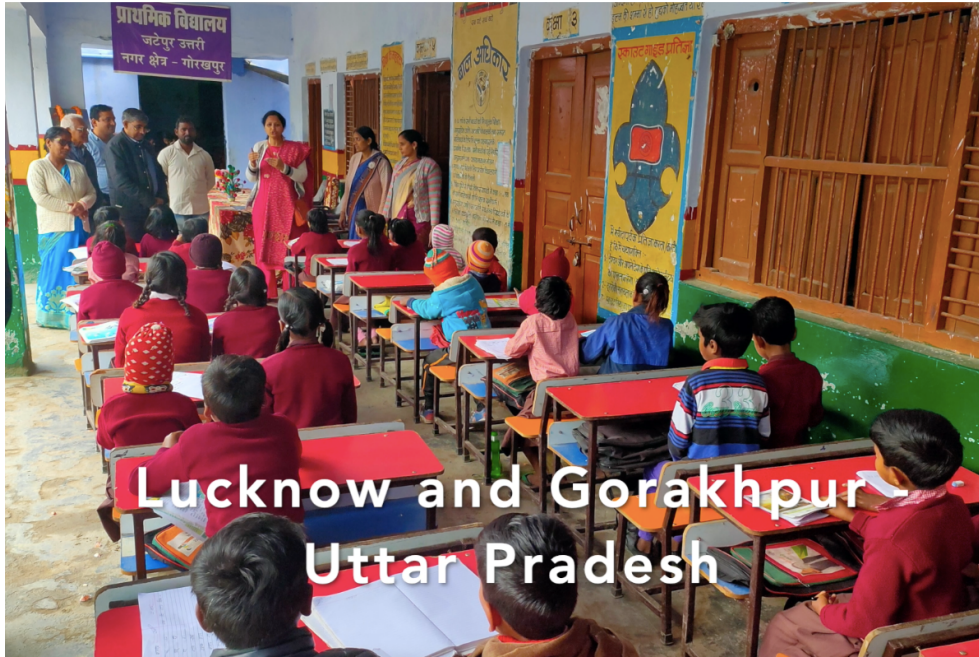

Thank You for supporting us,
Sewa T&H Team
www.toilets-sewausea.org
