




BC Wire Rope & Rigging
2720 E. Regal Park Drive
Anaheim, CA 92806

CERTIFICATE OF TESTING

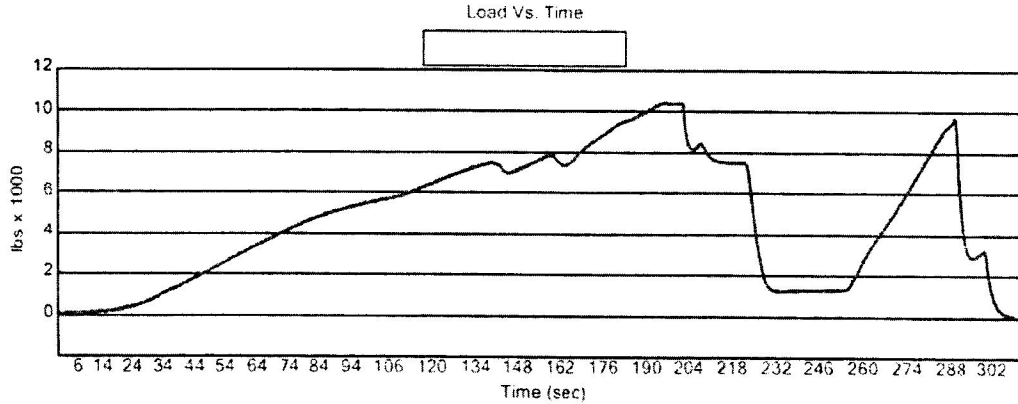

Test Date: 11/7/2016

Test Duration (HH:MM:SS): 00:05:09

Test Report #: 50

Peak Load (lbs x 1000): 10.43

Material Description: C/F 1/2" X 3.9" HIGH SPEED ROPE DIAMOND SNATCH BLOCK W/
WICHARD 1405 & 1/2" KERNMANTLE ROPE; BOWLINES BOTH
ENDS

Serial Number: #2

Notes: PULL TEST TO DESTRUCTION

Customer: SWEENY

Customer PO#: N/A

Sales Order #: 340703

Operator: JESUS T

Quality Control:

These products have had a load applied to them in conformance with the customer's specifications. There are no warranty, expressed or implied, by the test machine manufacturer that these goods are suitable for a purpose or use

Datatest Software Copyright © 2006 Chant Engineering Co. Inc.

Page 1 of 1 on 11/7/2016 1:45:27 PM

NOTES:

ROPE FAILED
