CLASSE 5 TWO GROUP S Compact models

Pre-Install Checklist

ELECTRICAL REQUIREMENTS:

Espresso Machine

**Voltage Range:** 208–240 VAC Single Phase
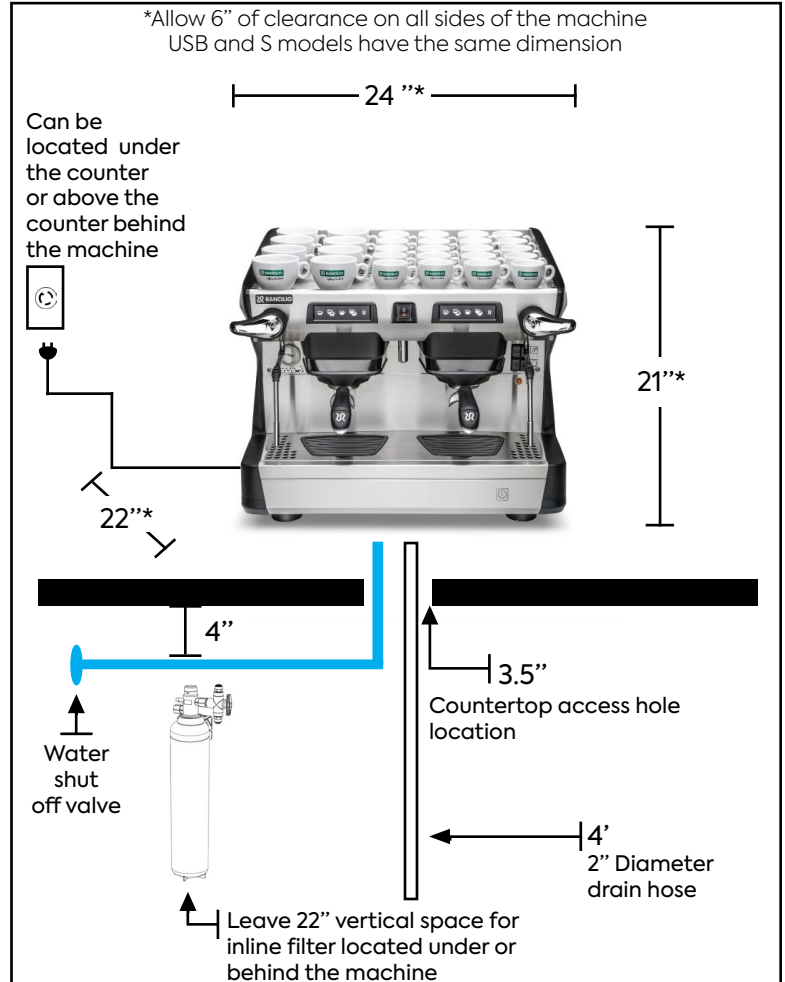
Watts: 3000

Circuit Size: 20 amps

SUGGESTED RECEPTACLE FOR ESPRESSO MACHINE:

NEMA 6–20R
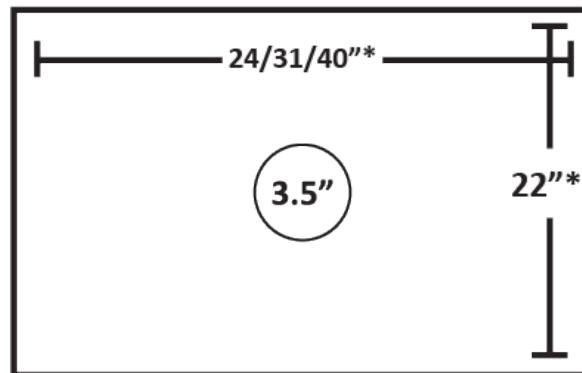

6–20R

PLEASE NOTE: Rancilio coffee machines do not use a neutral line. A dedicated ground wire is required for proper performance.

*Allow 6" of clearance on all sides of the machine
USB and S models have the same dimension

24 "*

Can be located under the counter or above the counter behind the machine

21"*

22"*

4"

Water shut off valve

3.5"
Countertop access hole location

4'
2" Diameter drain hose

Leave 22" vertical space for inline filter located under or behind the machine

DRILLING PLAN

24/31/40"*

3.5"

22"*

(front)

CLASSE 5 TWO GROUP S Compact models

Pre-Install Checklist

WATER REQUIREMENTS:

Dedicated cold water access line with standard female 3/8" NPT fitting and manual shut-off valve within 4' of the machine.

Water entering the machine should have a water hardness level of 2-3 GPG at all times.

Line pressure of water going to the machine should be between 30-70psi. If it is not consistently within this range, please install a pressure regulator.

DRAIN REQUIREMENTS:

Open gravity drain with minimum 2" I.D., within 4' of the machine.

SPACE REQUIREMENTS:

Allow at least 6" of clearance on all sides of the machine.

Allow 24" x 5" of space for in-line filter. Filter can be mounted behind the machine or under the counter.

COFFEE REQUIREMENTS:

On installation day, you must have 2 lbs of each type of coffee you are serving (i.e. 2 lbs of regular and 2 lbs of decaf coffee beans).

Sign and return via fax to Rancilio Group North America at 630-914-7901 or print, sign, scan and email to servicecoordinator@ranciliogroupna.com.

By signing, you agree to the following:

- If the installer arrives and the site is not ready, pre-payment of $500 must be issued to Rancilio before a second installation attempt will be made.
- Installation must be completed by a certified technician with written permission from Rancilio.
- You have read and understood this Pre-install Checklist.
- You are aware of the requirements needed for the installation.

Failure to comply will void all warranty and maintenance packages.

Full Name*

_____

Company Name*

_____

Email*

_____

Phone*

_____

Address/Site Location*

_____

Signature*

_____

Date*

_____

*Required information

CL 5 2G Compact 220V 01.22.2020
